Fall Brook Elementary School

Leominster, MA

Fall Brook Building Committee Meeting #17

September 10, 2024

LeftField

MDS ARCHITECTS

TODAY'S AGENDA

1. Call to Order & Roll Call
2. Administrative Actions
    a. Previous Meeting Minutes – **Vote**
    b. Review Invoice Log
    c. Warrant – **Vote**
    d. Budget Update
    e. Project Schedule Update
    f. MA Office of Campaign and Political Finance
3. Designer Report
    a. Facilities Assessment Subcommittee
    b. Mass Save Incentives
4. Items Not Anticipated 48 Hours in Advance of Meeting
5. Public Comment
6. Next Steps
7. Adjournment

ROLL CALL

- Seven (7) voting members are required for a quorum.

Voting Member	Present	Absent
Mr. Peter Angelini		
Mr. Mark Bodanza		
Mr. Greg Chapdelaine		
Mr. Bill Charpentier		
Ms. Robin Desmond		
Mr. Steven Mammone		
Mayor Dean Mazzarella, Chair		
Ms. Melanie Mikels		
Mr. Elliot Nadeau		
Mr. Raymond Racine		
Ms. Jennifer Reddington		
Mr. Brandon Robbins		
Mr. Jeffrey Sullivan		

TODAY'S AGENDA

1. Call to Order & Roll Call
2. Administrative Actions
   a. Previous Meeting Minutes – **Vote**
   b. Review Invoice Log
   c. Warrant – **Vote**
   d. Budget Update
   e. Project Schedule Update
   f. MA Office of Campaign and Political Finance
3. Designer Report
   a. Facilities Assessment Subcommittee
   b. Mass Save Incentives
4. Items Not Anticipated 48 Hours in Advance of Meeting
5. Public Comment
6. Next Steps
7. Adjournment

MEETING MINUTES FOR APPROVAL

- “Motion to approve the August 27, 2024, meeting minutes”, made by _____, seconded by _____.
- Discussion
- Vote

Voting Member	Yea	Nay	Abstain	Absent
Mr. Peter Angelini				
Mr. Mark Bodanza				
Mr. Greg Chapdelaine				
Mr. Bill Charpentier				
Ms. Robin Desmond				
Mr. Steven Mammone				
Mayor Dean Mazzarella, Chair				
Ms. Melanie Mikels				
Mr. Elliot Nadeau				
Mr. Raymond Racine				
Ms. Jennifer Reddington				
Mr. Brandon Robbins				
Mr. Jeffrey Sullivan				

INVOICE LOG

MEMORANDUM

To: Gregory Chapdelaine, Purchasing Agent

From: Linda Liporto, LeftField, LLC

Date: September 3, 2024

Re: Fall Brook Elementary School - August 2024 Invoice Summary

Cc: Craig DiCarlo, LeftField, LLC

Enclosed for approval and processing, please find the following invoices:

INVOICES (Payments)					
ProPay Code	**Vendor**	**Invoice #**	**Budget Category**	**Description of Services**	**Invoice $**
0001-0000	LeftField, LLC	2023.009-015	OPM Feasibility Study/Schematic Design	FS Phase Project Management Services for August 2024	$ 22,056.00
0002-0000	MDS	0069621	A&E Feasibility Study/Schematic Design	FS Phase Designer Services for August 2024	$ 61,219.70
				TOTAL:	**$ 83,275.70**

The invoices listed above are consistent with the Total Project Budget and to the best of our knowledge, are eligible for reimbursement from the Massachusetts School Building Authority. Leftfield, LLC recommends that the invoices be approved and paid.

The August 2024 OPM Monthly Report was electronically submitted to the MSBA and to the City of Leominster by the required September 12, 2024 deadline. All invoices above are included in the August 2024 Project Budget Report but can be revised if rejected by the City of Leominster.

If you have any questions, please feel free to contact Linda Liporto, Owner's Project Manager, Leftfield, LLC.

INVOICE LOG

INVOICES (Payments)					
ProPay Code	**Vendor**	**Invoice #**	**Budget Category**	**Description of Services**	**Invoice $**
0001-0000	LeftField, LLC	2023.009-015	OPM Feasibility Study/Schematic Design	FS Phase Project Management Services for August 2024	$ 22,056.00
0002-0000	MDS	0069621	A&E Feasibility Study/Schematic Design	FS Phase Designer Services for August 2024	$ 61,219.70
				TOTAL:	**$ 83,275.70**

WARRANT

A/P VOUCHER TRANSMITTAL FORM

CITY OF LEOMINSTER, MA.

FY25

WARRANT NUMBER: W08FY25
WEEK ENDING: 8/22/2024

VENDOR NUMBER	Vendor Name	ACCOUNT NUMBER		AMOUNT	School	School Dept. Use Only	
		ORG CODE	OBJECT			SCHL P.O.#	INVOICE #
37733	*LeftField, LLC*	3205300	530500	$ 22,056.00	FALL		2023.009-014
40967	*MDS*	3205300	530500	$ 105,525.25	FALL		0069572
			TOTAL	$ 127,581.25			

DRAFT

I/we hereby certify that the supplies and/or services as shown on the bills enclosed in this voucher have been received by this department in quantity and quality as ordered. The prices have been verified and that the above amounts are due and hereby approved for payment. The above statements are made under the penalties of perjury.

Signature: _____ _____ _____

Title: Mayor | Superintendent of Schools | Business Manager

WARRANT APPROVAL

VENDOR NUMBER	Vendor Name	ACCOUNT NUMBER		AMOUNT	School	School Dept. Use Only	
		ORG CODE	OBJECT			SCHL P.O.#	INVOICE #
37733	*LeftField, LLC*	3205300	530500	$ 22,056.00	FALL		2023.009-014
40967	*MDS*	3205300			FALL		0069572
			TOTAL	$ 127,581.25			

DRAFT

WARRANT APPROVAL

- “Motion to approve warrant number W12FY25 in the amount of $83,275.70” made by _____, seconded by _____.
- Discussion
- Vote

Voting Member	Yea	Nay	Abstain	Absent
Mr. Peter Angelini				
Mr. Mark Bodanza				
Mr. Greg Chapdelaine				
Mr. Bill Charpentier				
Ms. Robin Desmond				
Mr. Steven Mammone				
Mayor Dean Mazzarella, Chair				
Ms. Melanie Mikels				
Mr. Elliot Nadeau				
Mr. Raymond Racine				
Ms. Jennifer Reddington				
Mr. Brandon Robbins				
Mr. Jeffrey Sullivan				

FEASIBILITY BUDGET

Fall Brook Elementary School - Leominster, MA — **August 31, 2024**

Total Project Budget Status Report

ProPay Code	Description	Total Project Budget	Authorized Changes	Revised Total Budget	Total Committed	% Cmtd to Date	Actual Spent to Date	% Spent to Date	Balance To Spend	Uncommitted	Comments
	FEASIBILITY STUDY AGREEMENT										
0001-0000	OPM Feasibility Study/Schematic Design	$ 1,000,000		$ 1,000,000	$ 397,000	40%	$ 297,756	30%	$ 99,244	$ 603,000	
0002-0000	A&E Feasibility Study/Schematic Design	$ 1,000,000	$ 66,535	$ 1,066,535	$ 1,066,535	100%	$ 522,669	49%	$ 543,866	$ -	BRR#1
0003-0000	Environmental & Site	$ 250,000		$ 250,000	$ 131,764	53%	$ 66,993	27%	$ 64,771	$ 118,236	
0004-0000	Other	$ 250,000	$ (66,535)	$ 183,465	$ -	0%	$ -	0%	$ -	$ 183,465	BRR#1
	SUB-TOTAL	**$ 2,500,000**	**$ -**	**$ 2,500,000**	**$ 1,595,299**	**64%**	**$ 887,418**	**35%**	**$ 707,881**	**$ 904,701**	
	TOTAL PROJECT BUDGET	**$ 2,500,000**	**$ -**	**$ 2,500,000**	**$ 1,595,299**	**64%**	**$ 887,418**	**35%**	**$ 1,612,582**	**$ 904,701**	

FUNDING SOURCES		
Maximum State Share	$ 1,852,500	74.1%
Minimum Local Share	$ 647,500	25.9%
SUB-TOTAL	**$ 2,500,000**	**100.0%**

CONSTRUCTION COST ESTIMATES	Date	Estimator	Amount	SF	Cost/SF
Designer FS Cost Estimate					
Designer SD Cost Estimate					
OPM SD Cost Estimate					
PFA Budget					

Feasibility Study Agreement Budget Transfers:

#1	FSA Amendment No.1	3/20/2024	Transfer $66,535 from Other to A&E FS/SD for Designer Contract

FEASIBILITY BUDGET

As of August 2024:

- Committed: 64%
- Expended: 35%

ProPay Code	Description	Total Project Budget	Authorized Changes	Revised Total Budget	Total Committed	% Cmtd to Date	Actual Spent to Date	% Spent to Date
	FEASIBILITY STUDY AGREEMENT							
0001-0000	OPM Feasibility Study/Schematic Design	$ 1,000,000		$ 1,000,000	$ 397,000	40%	$ 297,756	30%
0002-0000	A&E Feasibility Study/Schematic Design	$ 1,000,000	$ 66,535	$ 1,066,535	$ 1,066,535	100%	$ 522,669	49%
0003-0000	Environmental & Site	$ 250,000		$ 250,000	$ 131,764	53%	$ 66,993	27%
0004-0000	Other	$ 250,000	$ (66,535)	$ 183,465	$ -	0%	$ -	0%
	SUB-TOTAL	$ 2,500,000	$ -	$ 2,500,000	$ 1,595,299	64%	$ 887,418	35%
	TOTAL PROJECT BUDGET	$ 2,500,000	$ -	$ 2,500,000	$ 1,595,299	64%	$ 887,418	35%

FEASIBILITY SCHEDULE

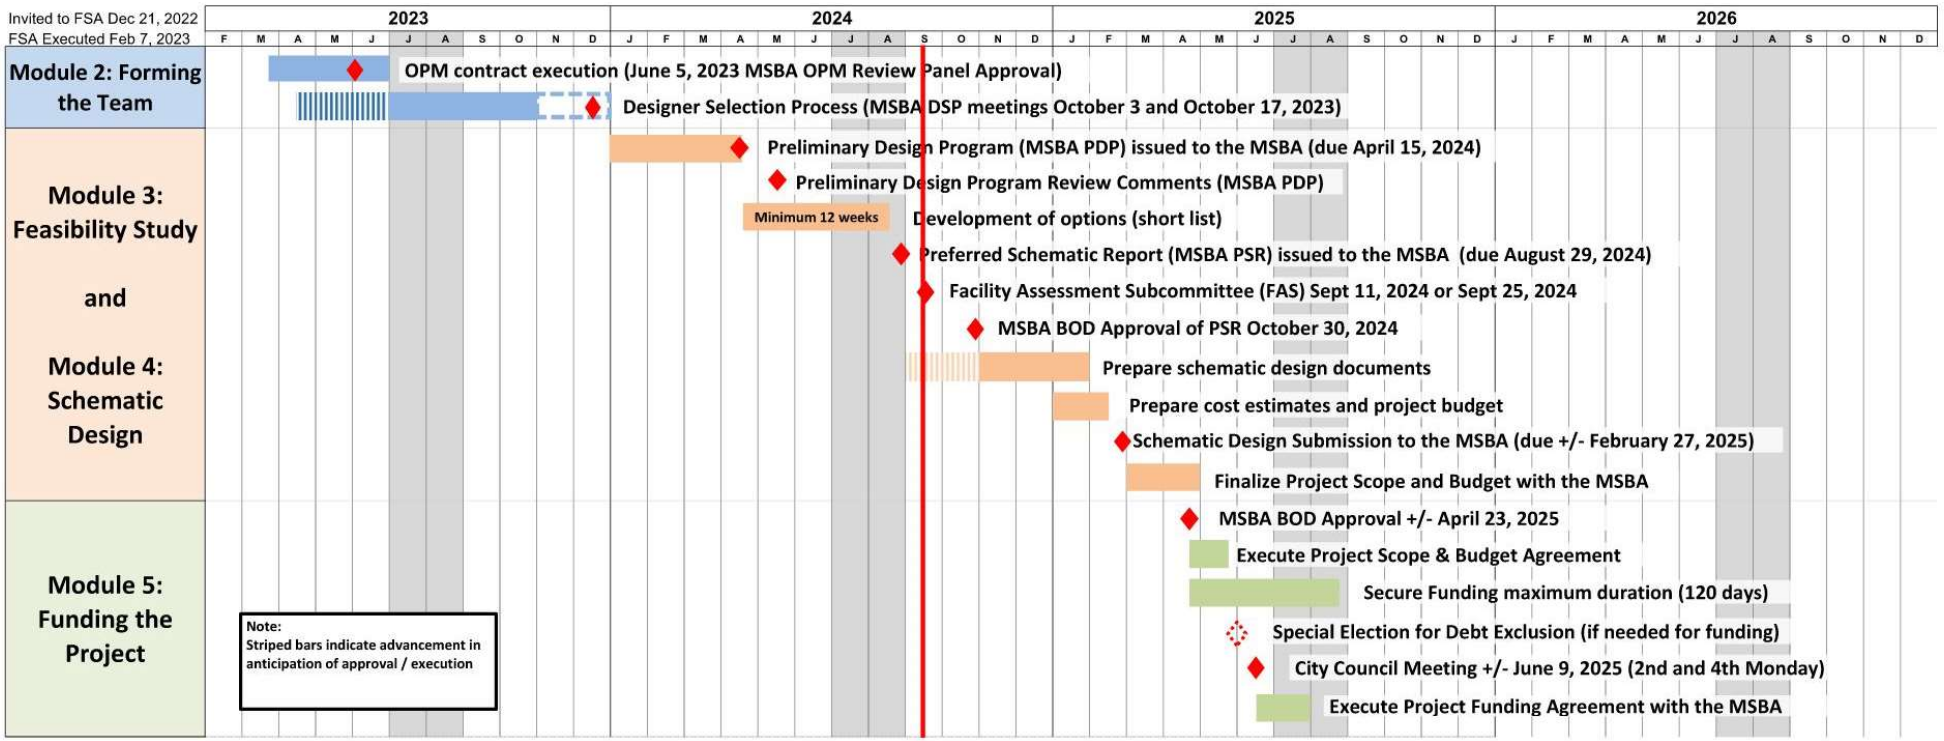

FEASIBILITY SCHEDULE

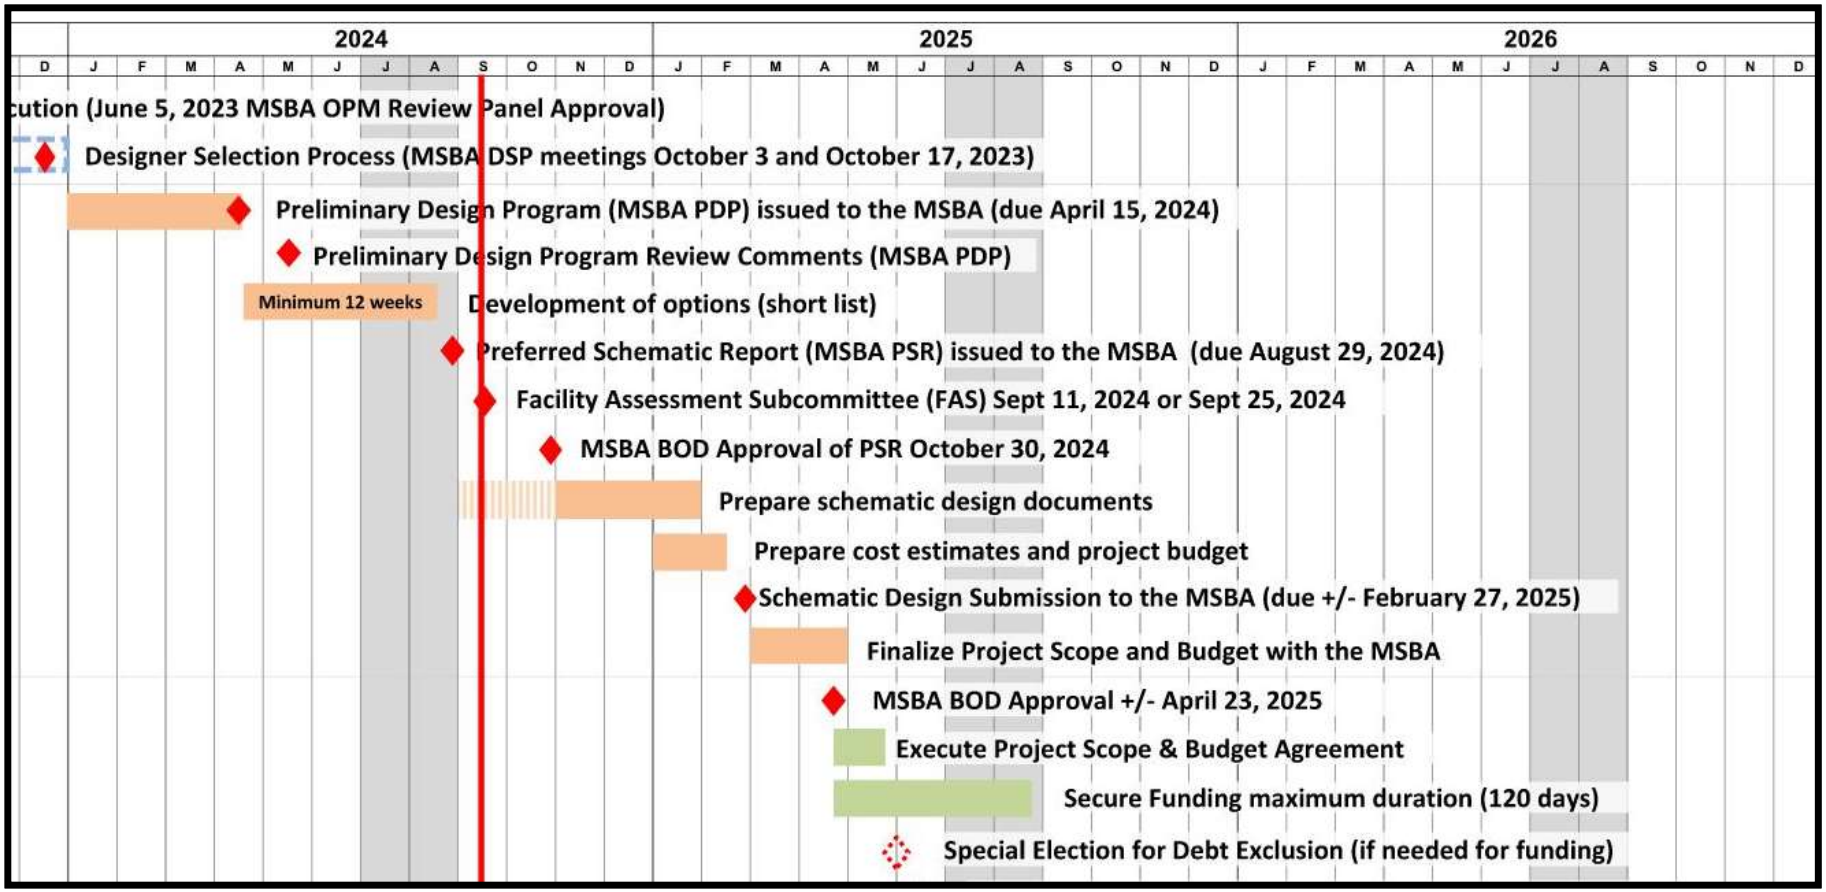

PRELIMINARY PROJECT SCHEDULE

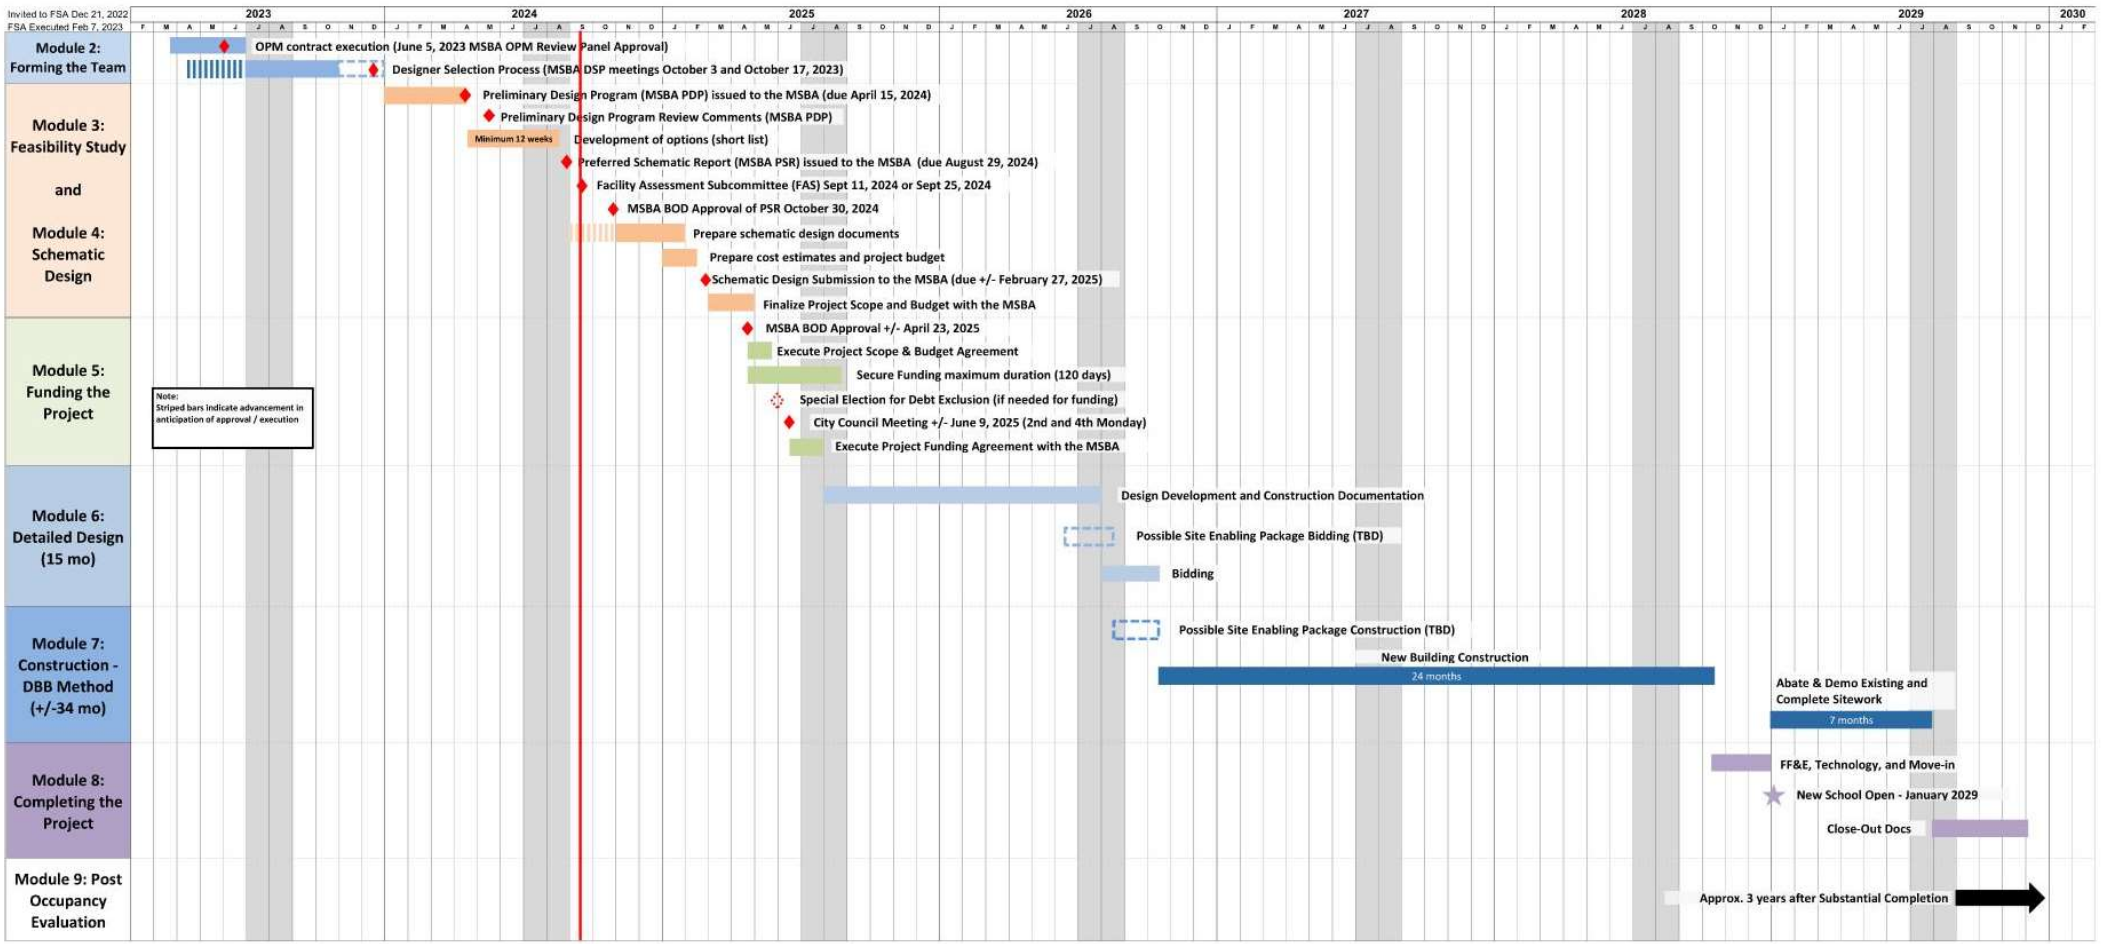

OFFICE OF CAMPAIGN & POLITICAL FINANCE

- MGL Ch. 55 Campaign Finance Law
- Law governing who can advocate for or against a ballot question and using public resources
- Political Action Committee (PAC), “Vote Yes” group
- Resource: Jason Tate

TODAY'S AGENDA

1. Call to Order & Roll Call
2. Administrative Actions
   a. Previous Meeting Minutes – **Vote**
   b. Review Invoice Log
   c. Warrant – **Vote**
   d. Budget Update
   e. Project Schedule Update
   f. MA Office of Campaign and Political Finance
3. Designer Report
   a. Facilities Assessment Subcommittee
   b. Mass Save Incentives
4. Items Not Anticipated 48 Hours in Advance of Meeting
5. Public Comment
6. Next Steps
7. Adjournment

DESIGNER REPORT

Switch to MDS presentation

MASS SAVE INCENTIVES

WE ARE MASS SAVE®:

BERKSHIRE GAS An AVANGRID Company · Cape Light Compact · EVERSOURCE · Liberty · nationalgrid · Unitil

MASS SAVE INCENTIVES

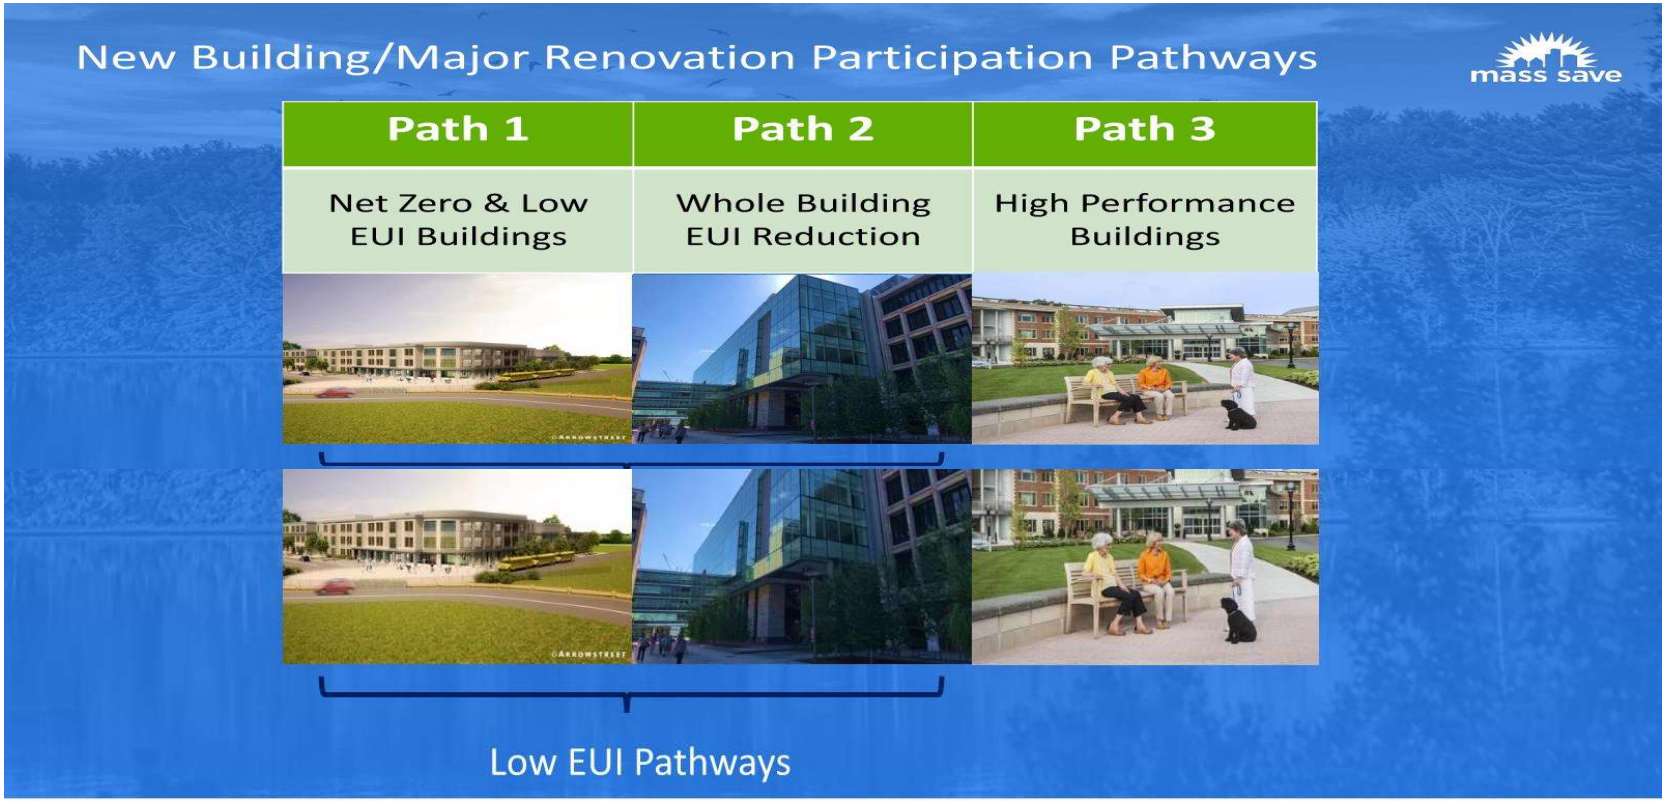

WE ARE MASS SAVE®:

BERKSHIRE GAS An AVANGRID Company

Cape Light Compact

EVERSOURCE

Liberty

nationalgrid

Unitil

MASS SAVE INCENTIVES

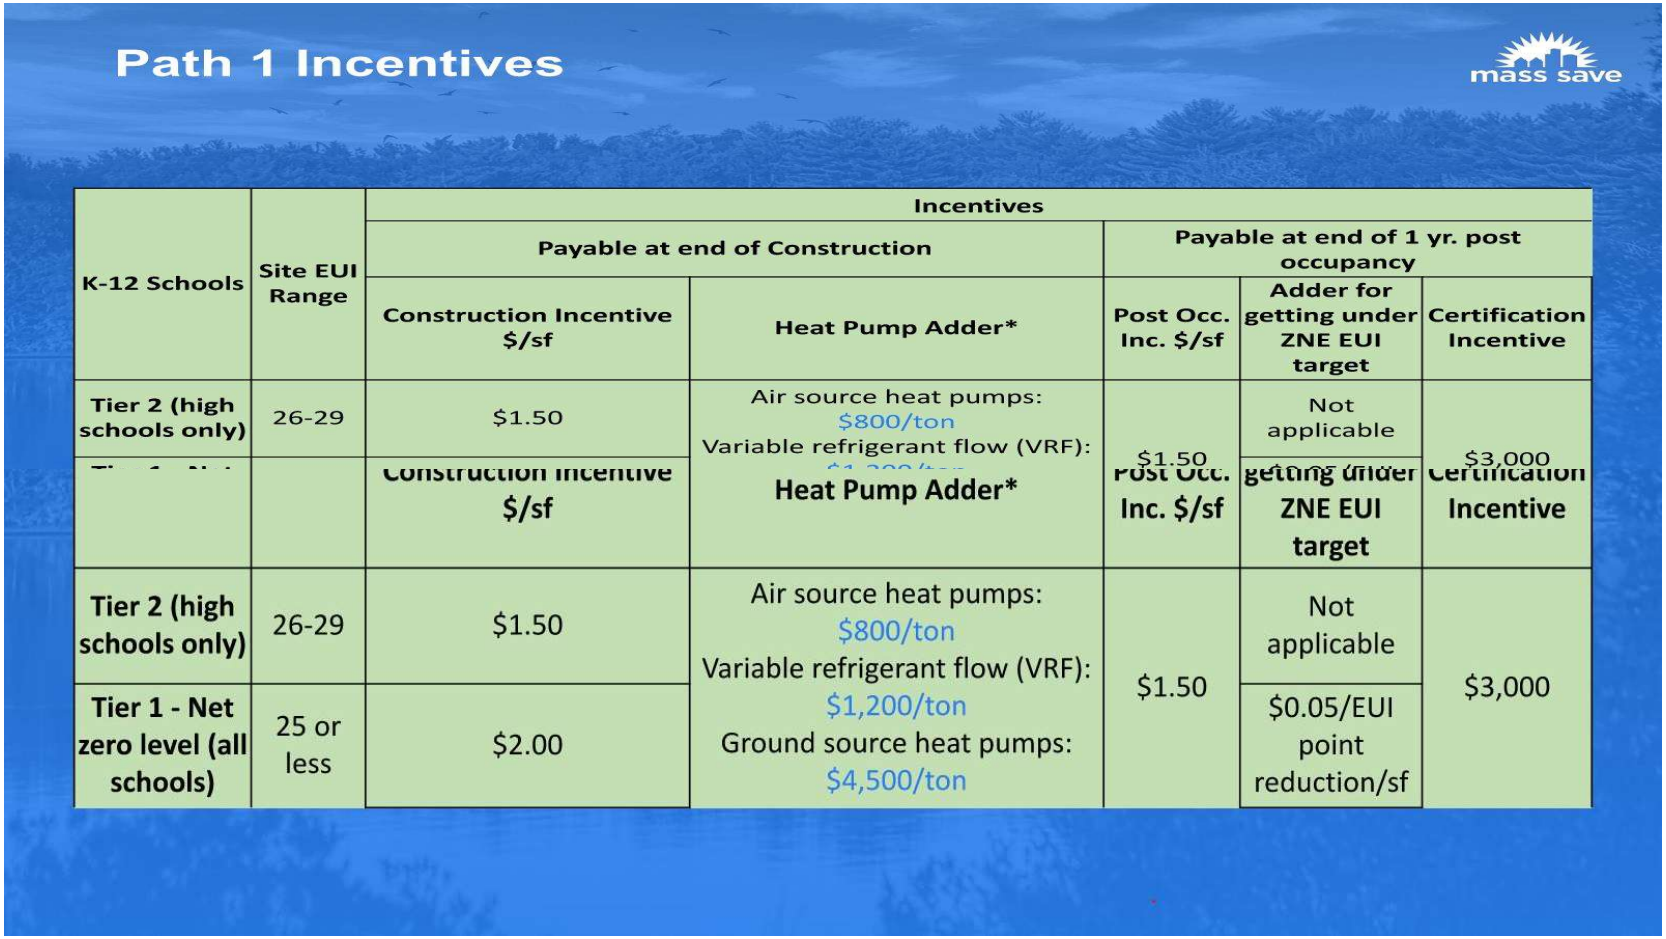

K-12 Schools	Site EUI Range	Incentives				
		Payable at end of Construction		Payable at end of 1 yr. post occupancy		
		Construction Incentive $/sf	Heat Pump Adder*	Post Occ. Inc. $/sf	Adder for getting under ZNE EUI target	Certification Incentive
Tier 2 (high schools only)	26-29	$1.50	Air source heat pumps: $800/ton Variable refrigerant flow (VRF):	$1.50	Not applicable	$3,000
Tier 1 - Net zero level (all schools)	25 or less	$2.00	Ground source heat pumps: $4,500/ton		$0.05/EUI point reduction/sf	

TODAY'S AGENDA

1. Call to Order & Roll Call
2. Administrative Actions
   a. Previous Meeting Minutes – **Vote**
   b. Review Invoice Log
   c. Warrant – **Vote**
   d. Budget Update
   e. Project Schedule Update
   f. MA Office of Campaign and Political Finance
3. Designer Report
   a. Facilities Assessment Subcommittee
   b. Mass Save Incentives
4. Items Not Anticipated 48 Hours in Advance of Meeting
5. Public Comment
6. Next Steps
7. Adjournment

TODAY'S AGENDA

1. Call to Order & Roll Call
2. Administrative Actions
   a. Previous Meeting Minutes – **Vote**
   b. Review Invoice Log
   c. Warrant – **Vote**
   d. Budget Update
   e. Project Schedule Update
   f. MA Office of Campaign and Political Finance
3. Designer Report
   a. Facilities Assessment Subcommittee
   b. Mass Save Incentives
4. Items Not Anticipated 48 Hours in Advance of Meeting
5. Public Comment
6. Next Steps
7. Adjournment

TODAY'S AGENDA

1. Call to Order & Roll Call
2. Administrative Actions
   a. Previous Meeting Minutes – **Vote**
   b. Review Invoice Log
   c. Warrant – **Vote**
   d. Budget Update
   e. Project Schedule Update
   f. MA Office of Campaign and Political Finance
3. Designer Report
   a. Facilities Assessment Subcommittee
   b. Mass Save Incentives
4. Items Not Anticipated 48 Hours in Advance of Meeting
5. Public Comment
6. Next Steps
7. Adjournment

NEXT STEPS

- Wed 9/11/24, 10:30am — MSBA FAS Meeting
- Tuesday 10/8/24, 1:00pm — Regular FBBC Meeting
- Wednesday 10/30/24, 10am — MSBA Board of Directors Meeting
- Tuesday 11/12/24, 1:00pm — Regular FBBC Meeting

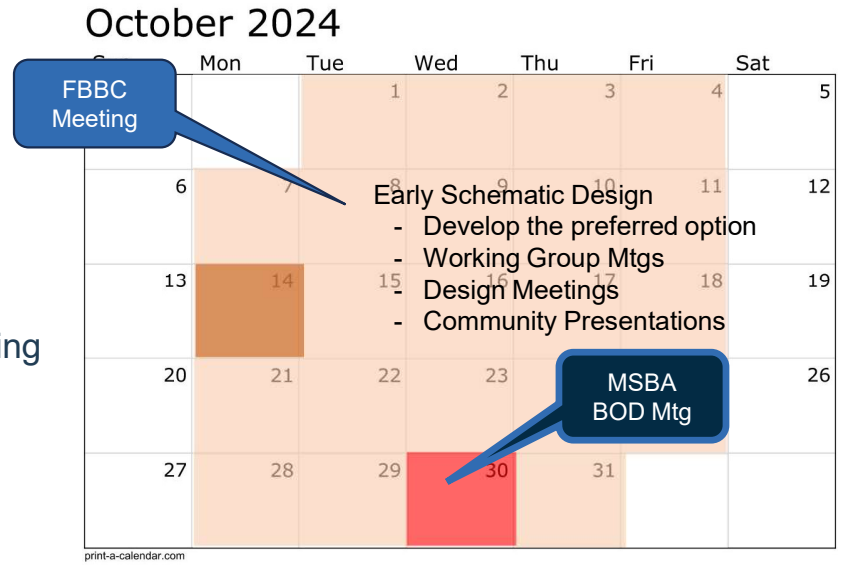

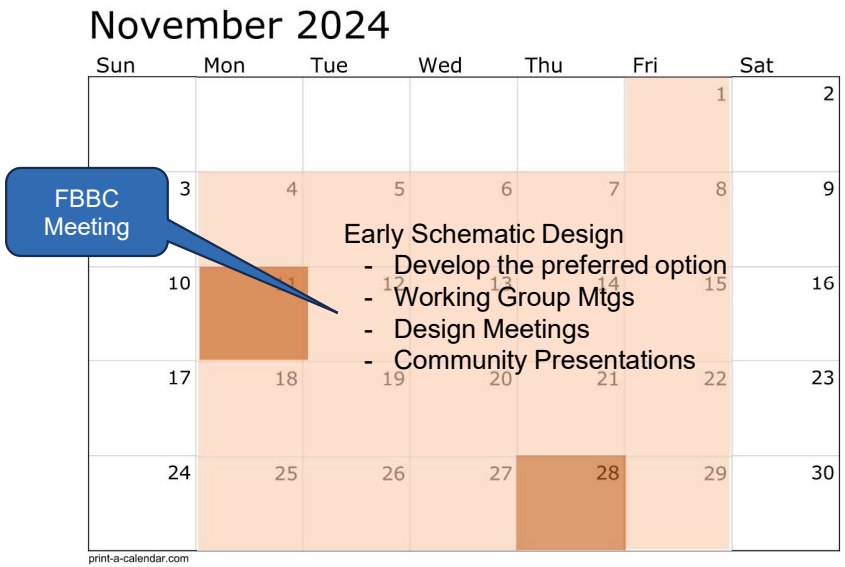

TODAY'S AGENDA

1. Call to Order & Roll Call
2. Administrative Actions
   a. Previous Meeting Minutes – **Vote**
   b. Review Invoice Log
   c. Warrant – **Vote**
   d. Budget Update
   e. Project Schedule Update
   f. MA Office of Campaign and Political Finance
3. Designer Report
   a. Facilities Assessment Subcommittee
   b. Mass Save Incentives
4. Items Not Anticipated 48 Hours in Advance of Meeting
5. Public Comment
6. Next Steps
7. Adjournment

ADJOURNMENT

- “Motion to adjourn” made by _____, seconded by _____.
- Discussion
- Vote

Voting Member	Yea	Nay	Abstain	Absent
Mr. Peter Angelini				
Mr. Mark Bodanza				
Mr. Greg Chapdelaine				
Mr. Bill Charpentier				
Ms. Robin Desmond				
Mr. Steven Mammone				
Mayor Dean Mazzarella, Chair				
Ms. Melanie Mikels				
Mr. Elliot Nadeau				
Mr. Raymond Racine				
Ms. Jennifer Reddington				
Mr. Brandon Robbins				
Mr. Jeffrey Sullivan				

THANK YOU!

LeftField

THE RIGHT CHOICE IN PROJECT MANAGEMENT

MDS ARCHITECTS
